


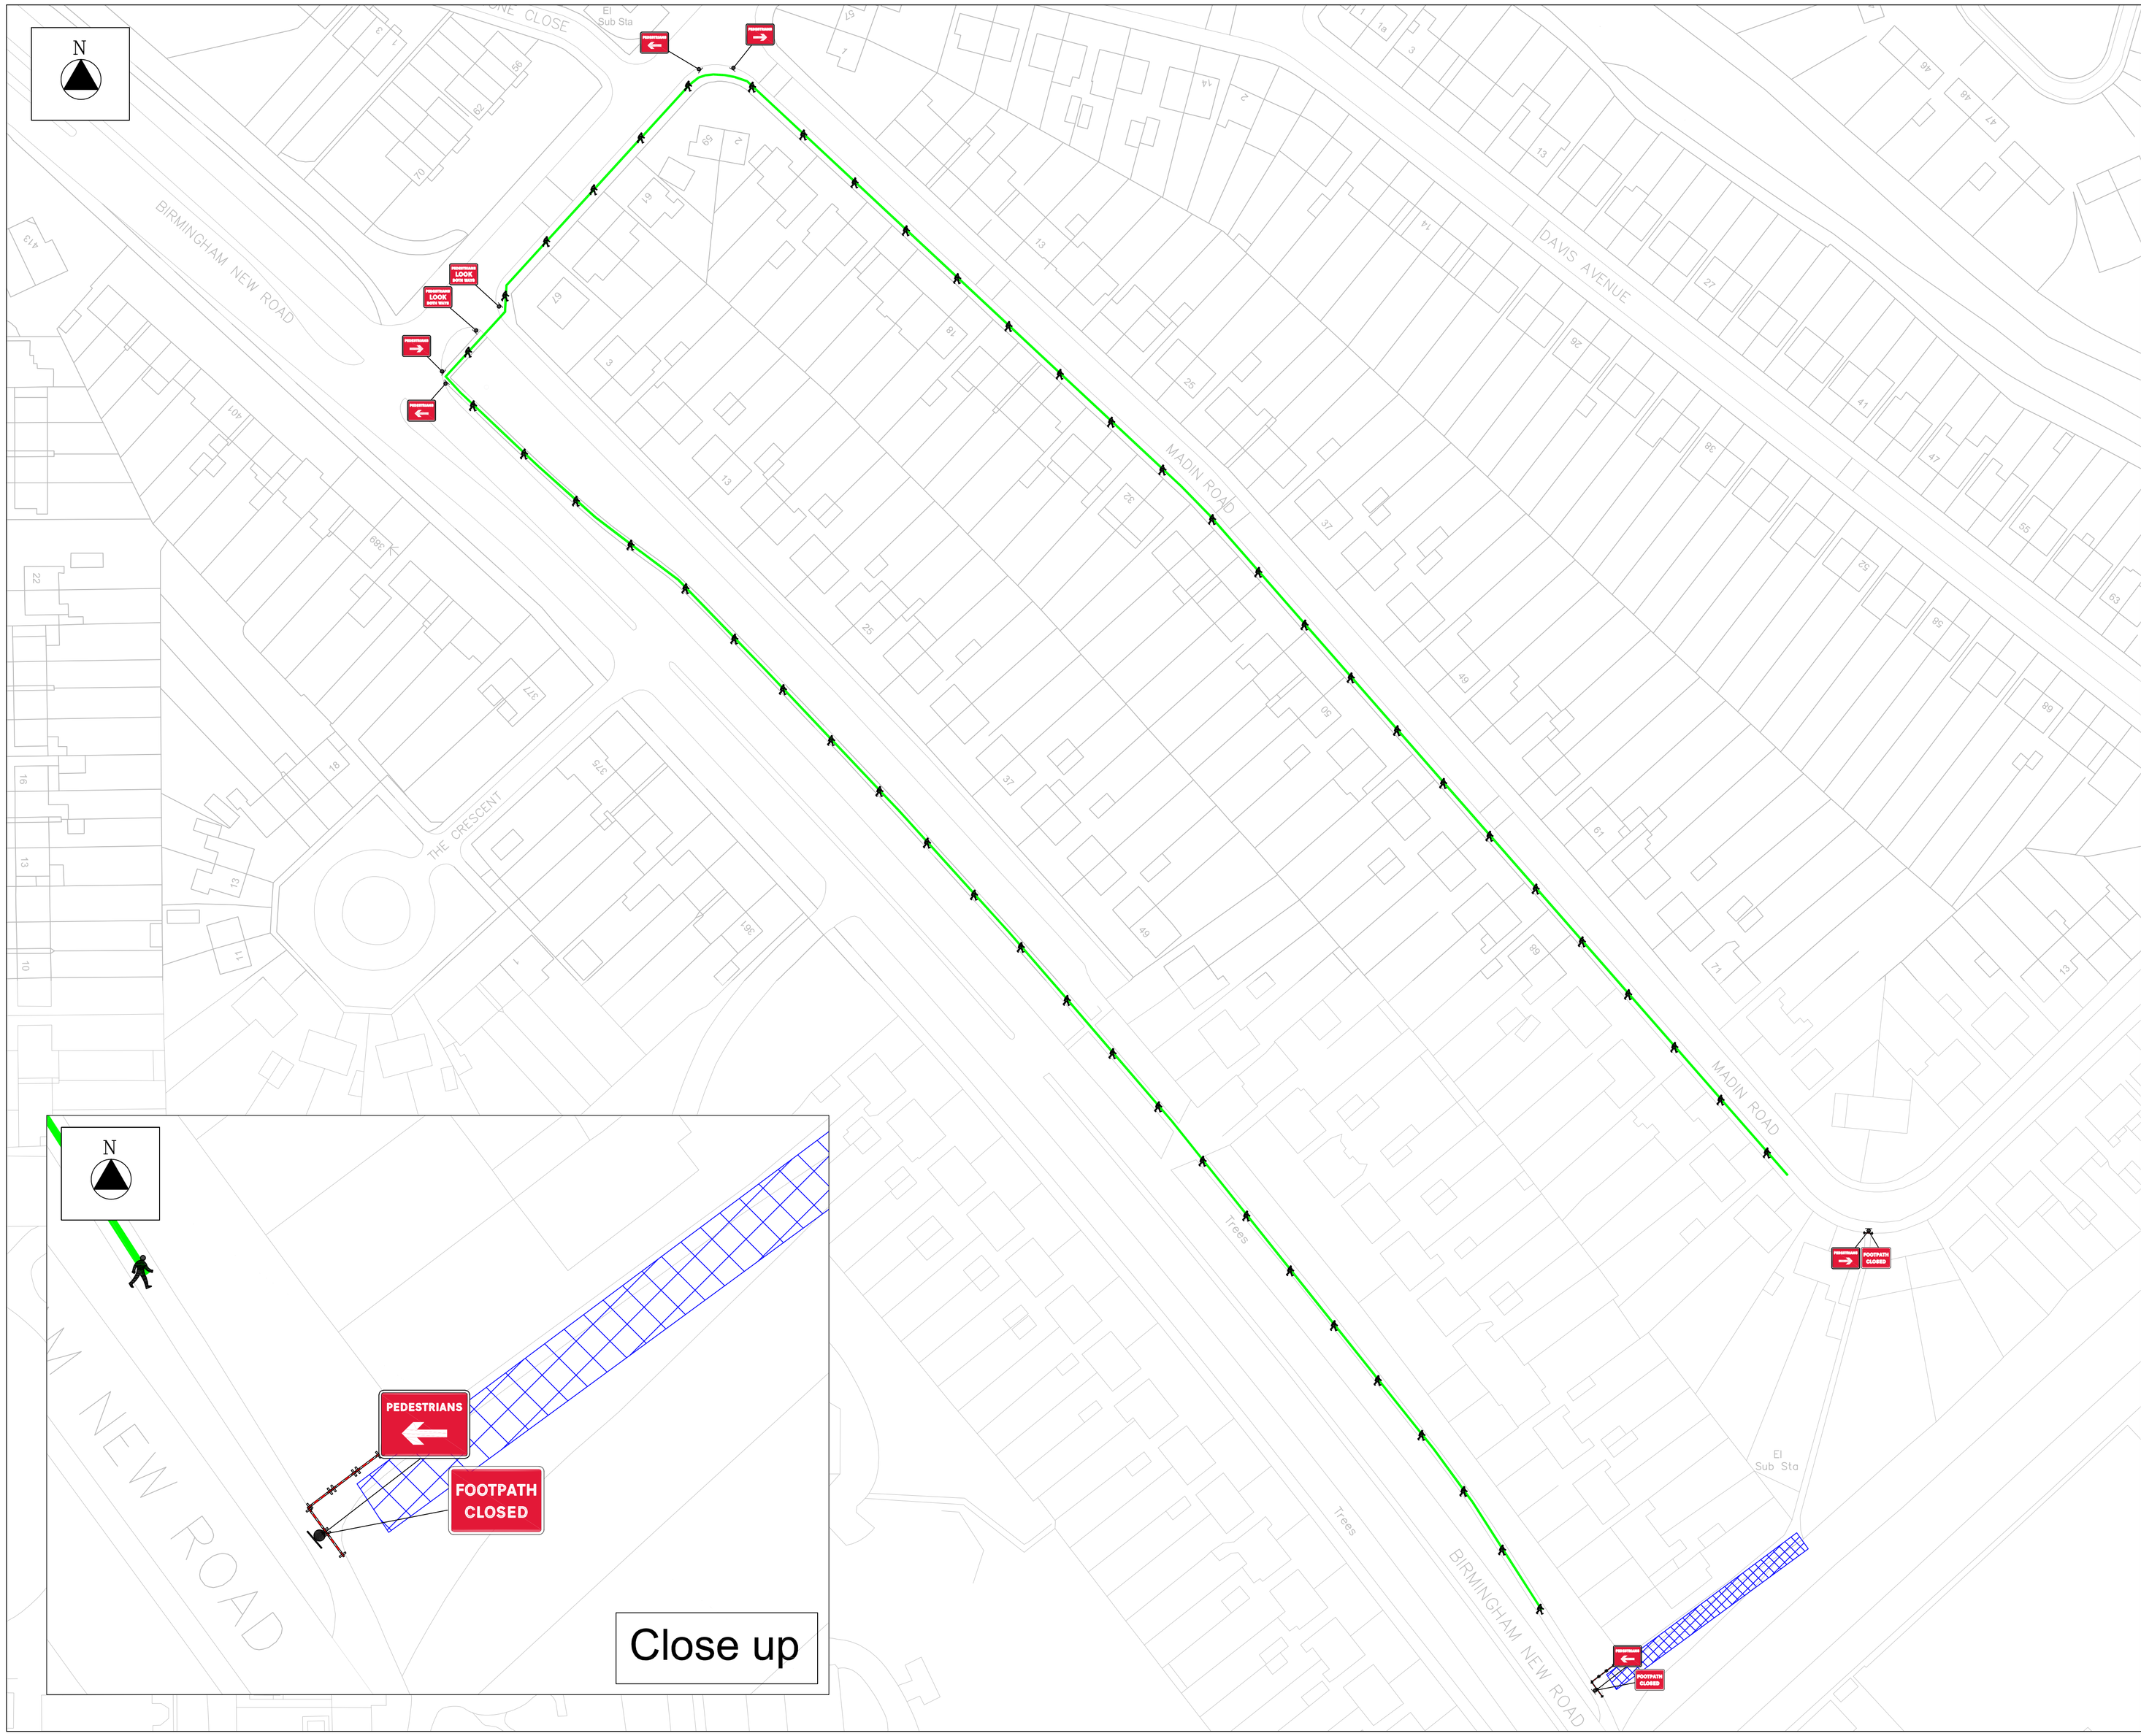


| Key | |
|---|---|
| | Traffic Sign |
| | Traffic Cone |
| B | Cone or Road Marking Detail |
| 610 | TSRGD Sign Reference Number |
| | Pedestrian Barrier |
| | Pedestrian Route |
| | Vehicle Diversion Route |
| | Hoarding / Heras |
| | Temporary Traffic Signal |
| | Temporary Traffic Signals |
| | Safety Zones |
| | New MMA Work Area |
| | Existing MMA Work Area |
| | Ramp |
| | MMA Marshal |
| | Cut Line |

Cone Detail

- No cone detail required.

## Grid Reference

| X (Eastings) - 000000 | Y (Northings) - 000000 |
|---|---|

Speed: 30

Safety Zones
(S) Sideways - 0.5m
(L) Longways - 0.5m
(C) Clearance - 2.0m

Notes

- Advance warning signs to be installed 2 weeks prior to footway closure.

All Traffic Management will be designed in accordance with the requirements of the Traffic signs Manual, Chapter 8, Part 1, Part 2 & Part 3. Any sign reference numbers used in this drawing refer to the diagram numbers contained within the Traffic Signs Regulations and General Directions 2016 (TSRGD 2016).

| Rev | Date | Revision Details | Drn | Des | Chk | App |
|---|---|---|---|---|---|---|
| P01 | 07/01/22 | checked and approved | JW | JW | AD | PV |
| P02 | 26/01/22 | checked and approved | JW | JW | AD | PV |

© Midland Metro Alliance

Midland Metro Alliance
4th Floor, Alpha Tower, Suffolk Street Queensway, Birmingham, B1 1TT
Tel: +44 (0)121 643 8729 www.metroalliance.co.uk

Project
Wednesbury to Brierley Hill

Drawing Title
Retaining Wall Repair Works
Lindley Avenue to
Birmingham New Road
Footpath Closure

| Scale | Drawn | Designed | Checked | Approved |
|---|---|---|---|---|
| N/A | JW | JW | AD | PV |
| Original Drawing Size: N/A (Not Applicable) | Date: 26/01/22 | Date: 06/01/22 | Date: 26/01/22 | Date: 26/01/22 |

Status Code: S4
Drawing Suitability: For Stage Approval

Drawing Number

| Project | Originator | Volume | Design Stg. |
|---|---|---|---|
| WBHD | D05 | TMN | C |

| Location | Type | Role | Number | Revision |
|---|---|---|---|---|
| ZZ | DR | TM | 0009 | P02 |
